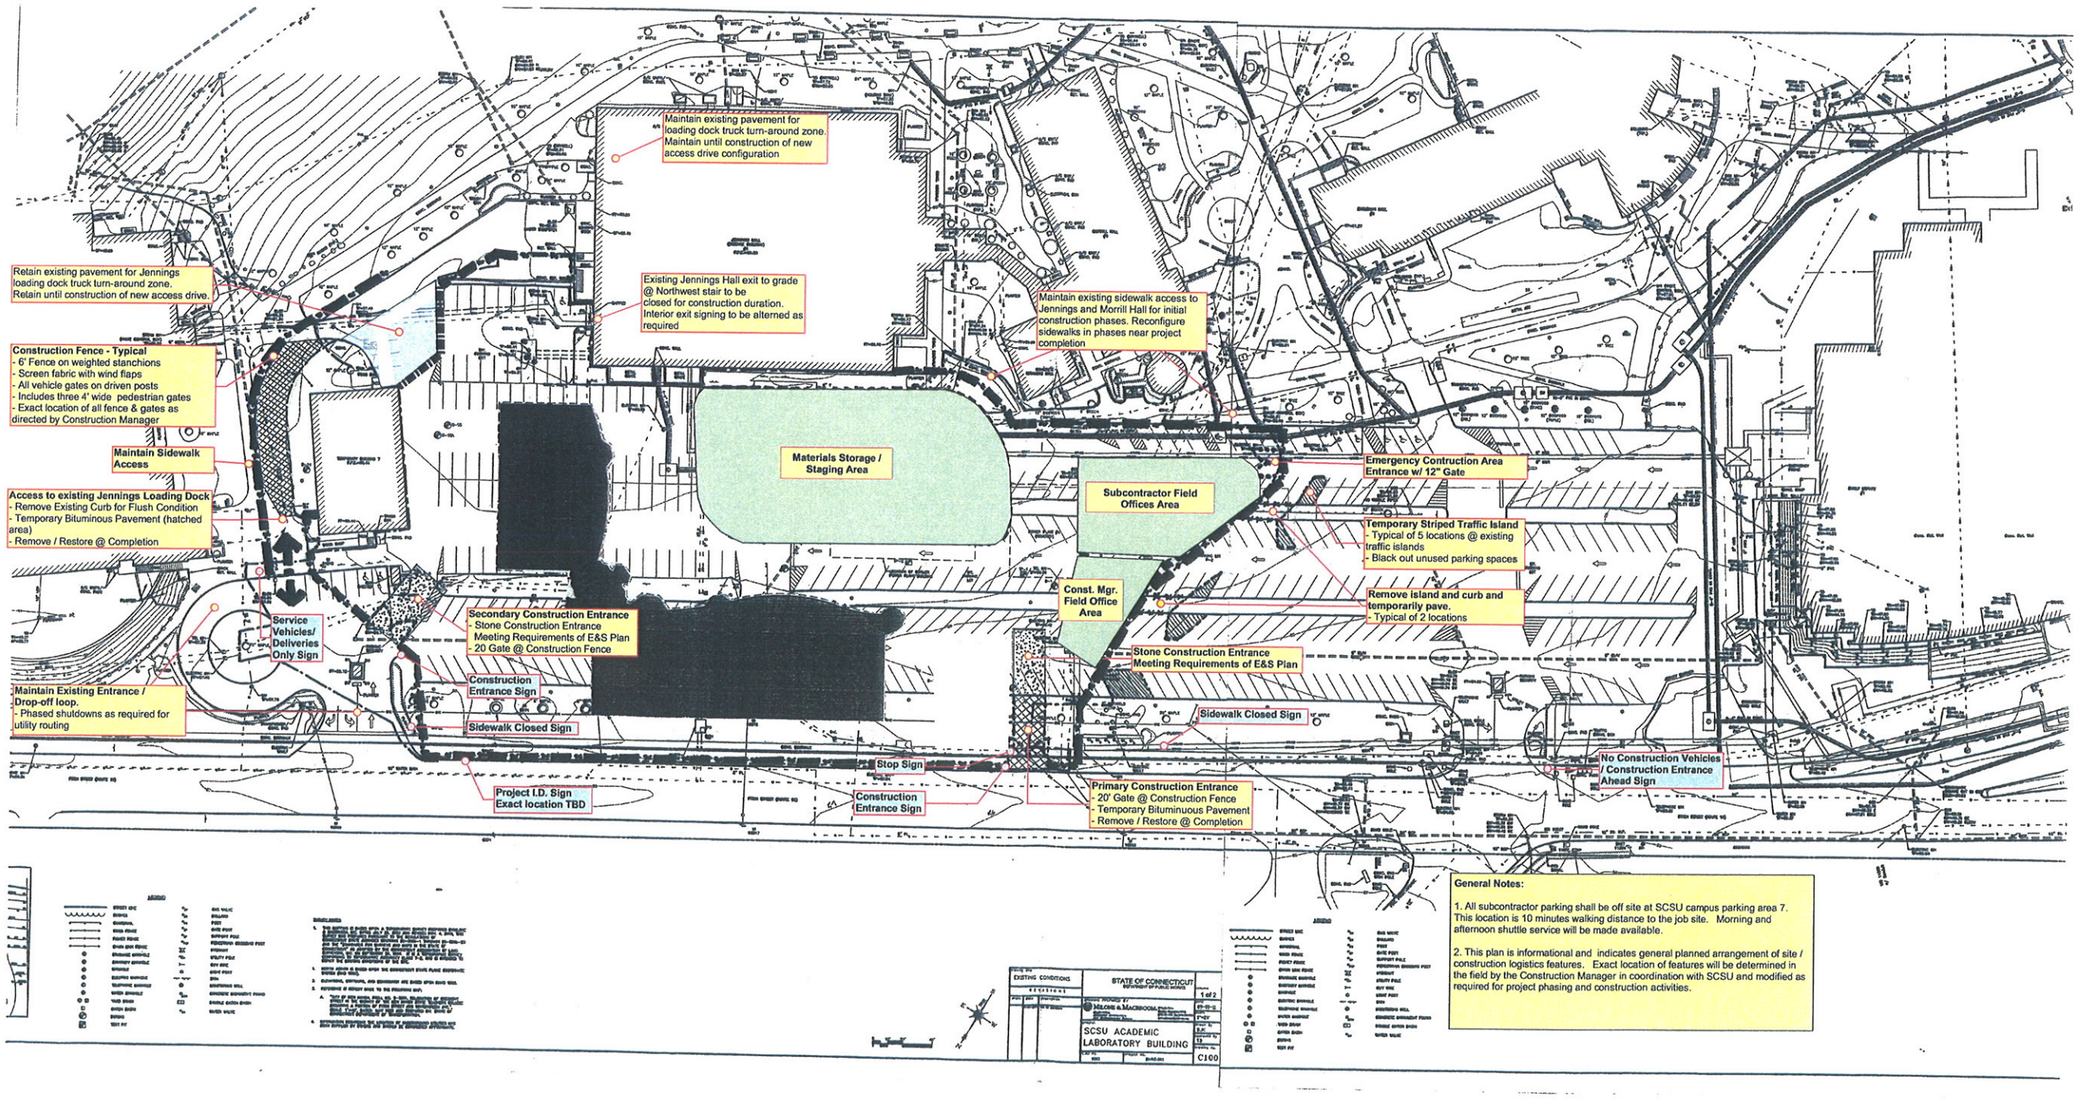
Maintain existing pavement for loading dock truck turn-around zone. Maintain until construction of new access drive configuration
Retain existing pavement for Jennings loading dock truck turn-around zone. Retain until construction of new access drive.
Existing Jennings Hall exit to grade @ Northwest stair to be closed for construction duration. Interior exit signing to be alterned as required
Maintain existing sidewalk access to Jennings and Morrill Hall for initial construction phases. Reconfigure sidewalks in phases near project completion
Construction Fence - Typical
- 6' Fence on weighted stanchions
- Screen fabric with wind flaps
- All vehicle gates on driven posts
- Includes three 4' wide pedestrian gates
- Exact location of all fence & gates as directed by Construction Manager
Maintain Sidewalk Access
Materials Storage / Staging Area
Subcontractor Field Offices Area
Emergency Contruction Area Entrance w/ 12' Gate
Temporary Striped Traffic Island
- Typical of 5 locations @ existing traffic islands
- Black out unused parking spaces
Access to existing Jennings Loading Dock
- Remove Existing Curb for Flush Condition
- Temporary Bituminous Pavement (hatched area)
- Remove / Restore @ Completion
Const. Mgr. Field Office Area
Remove island and curb and temporarily pave.
- Typical of 2 locations
Service Vehicles/ Deliveries Only Sign
Secondary Construction Entrance
- Stone Construction Entrance Meeting Requirements of E&S Plan
- 20 Gate @ Construction Fence
Stone Construction Entrance Meeting Requirements of E&S Plan
Construction Entrance Sign
Maintain Existing Entrance / Drop-off loop.
- Phased shutdowns as required for utility routing
Sidewalk Closed Sign
Sidewalk Closed Sign
Stop Sign
No Construction Vehicles / Construction Entrance Ahead Sign
Project I.D. Sign Exact location TBD
Construction Entrance Sign
Primary Construction Entrance
- 20' Gate @ Construction Fence
- Temporary Bituminous Pavement
- Remove / Restore @ Completion
EXISTING CONDITIONS
STATE OF CONNECTICUT
SCSU ACADEMIC LABORATORY BUILDING
C100
General Notes:
1. All subcontractor parking shall be off site at SCSU campus parking area 7. This location is 10 minutes walking distance to the job site. Morning and afternoon shuttle service will be made available.
2. This plan is informational and indicates general planned arrangement of site / construction logistics features. Exact location of features will be determined in the field by the Construction Manager in coordination with SCSU and modified as required for project phasing and construction activities.
